ATE SOLUTIONS B.V.

BUDGET QUOTATION Q-2025-001

Date: 23-05-2025

Supplier: ATE Solutions B.V.
Oude Telgterweg 255
3853PG, ERMELO
0031 085-0410183
info@atesolutions.nl
VAT no. NL 8656 38792 B01
C.o.c. no. 91385415
IBAN: NL28INGB 0102962979
The Netherlands

Customer: Friendship flowers
Ethiopia

Quotation description: Utilities for new farm
Revision: V1.1

Information

Project description:
The client has requested a budget quotation for the electrical installation on their new flower farm.
The information received at this stage is as followed:
- Everything build in plug and play containers, this to get the equipment up and running in a short time frame.
- Customer suggest the next power sources. After creating a load list this can be confirmed.
  - 350KVA Generator
  - 660KVA Generator
- Load listfrom customer state a Total installed capacity of 550KW with a peakload of 280KW from 8:00 till 11:00.
- Setup should be constructed in such a way that it delays or prevents theft and arson during incidents of civil unrest.

Extra project information:
We often find it advisable to deliver a complete installation. Therefore, we also offer an MV (Medium Voltage) installation and a voltage stabilizer.

For the MV installation we go with 800KVA at 15kV. Ring Main Unit with Vaccum Circuit breaker and 2 fields. Including surrge arrestors and drop out fuses. All underground cabling, starting from the fuses included. This is not corrosponding with the 660KVA geenerator unless selection is made with future expansion in mind.

For the Voltage stabilizer we have included two options:
1. Mechanical stabilizer – ±15% correction range. Not suitable for synchronization. Correct sercice and maintaince on a weekly base is increasing the lifetime.

2. Static stabilizer with battery backup – 20% correction range. Capable of handling peak loads. Modular and easily expandable. Ensures uninterrupted power supply during switching between generator and grid.

Farm layout:
During detail engineering we expect that a change in the setup of the power distribution on the farm will be made for the best combination between cost efficientie en reliability.

Functioning:
The equipment will work fully automatic. With an option to switch to manual operation. The 'brain' will be the Main Distribution Board which will be equiped with a Siemens PLC. During commisining a programmer will be available to programm the logics requered by the customer. The MDB have the possibilty to switch any breaker on or off in the case of the smaller generator operating.

Continuation:
Given the early stage of the project, there is a significant amount of missing information, which currently precludes us from conducting comprehensive calculations and designs.
When entering a partnership, we can explore various options together. Additionally, we see further opportunities to mitigate the investment to some extent. The client may also express interest in investigating green energy alternatives or solutions that substantially reduce operational costs.
The prices listed below are provided as estimates and are subject to change.

ATE SOLUTIONS B.V.

BUDGET QUOTATION Q-2025-001

Date: 23-05-2025

Position	Description	Quantity	Unit Price:	Total Price:
010	Transformer 800KVA 15kV/0,4kV with RMU and LV panel	1 Pcs.	€ 104.000,00	€ 104.000,00
020	MV installation items, Fuses, Cabling (100M), Surge arrestors	1 Set	€ 27.200,00	€ 27.200,00
030	Diesel generator 640KVA, Scania / Leroy Sommer	1 Pcs.	€ 85.500,00	€ 85.500,00
031	Diesel generator 650KVA, Baudouin / Leroy Sommer	1 Pcs.	€ 73.500,00	€ 73.500,00
040	Voltage stabilizer servo operated +/- 15%	1 Pcs.	€ 76.500,00	€ 76.500,00
041	Ups with voltage stabilisation +/-20%	1 Set	€ 116.400,00	€ 116.400,00
050	Diesel generator 355KVA, Scania / Leroy Sommer	1 Pcs.	€ 57.000,00	€ 57.000,00
051	Diesel generator 350KVA, Baudouin / Leroy Sommer	1 Pcs.	€ 46.500,00	€ 46.500,00
060	Main distribution board, 1600A, with S7-1200 PLC	1 Pcs.	€ 70.000,00	€ 70.000,00
070	Assambled and installed 40ft container 1	1 Pcs.	€ 35.000,00	€ 35.000,00
080	Assambled and installed 40ft container 2	1 Pcs.	€ 30.000,00	€ 30.000,00
090	Cables and connection materials	1 Set	€ 0,01	€ 0,01
100	Installation costs	1 Set	€ 36.000,00	€ 36.000,00
		Total:		€ 757.600,01

Amount in words:

Detail engineering:
The next drawings will be hand over before start of production:
- Farm layout (Top view)
- 40Ft container design. (3D design, PDF's will be hand over for approval.)
- Load list (Excel)

After shipment the next drawings will hand over for prepatory installation works:
- Container stands
- Cable trenches

There will be additional drawings during detail engineering to have a correct understanding of the customer needs.

ATE SOLUTIONS B.V.

BUDGET QUOTATION Q-2025-001

Date: 23-05-2025

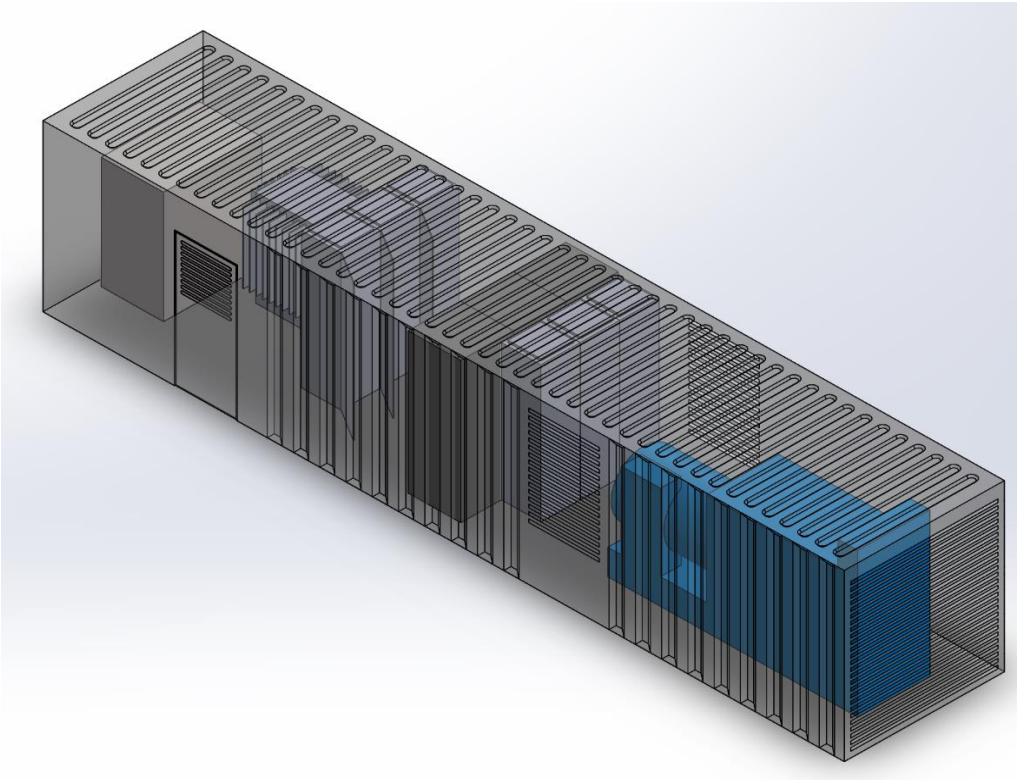

Budget quotation:
This budget quotation provides a comprehensive overview of the costs involved. Please note that no rights can be derived from this budget quotation. The exact price for the project will be provided upon completion of detailed engineering.

Payment conditions: 70% at order, 20% before shipment, 10% after SAT signed.
Delivery: Ex Works
Delivery time: To be discussed (+/- 12 weeks)
Validity: 30 Days

Kind regards, A. Tomassen
